



## Project Initiation Document

### PROJECT DETAILS

|                        |                                                             |
|------------------------|-------------------------------------------------------------|
| <b>DOCUMENT NUMBER</b> | PID _2017_ < EQUITY BANK TANZANIA VODACOM >                 |
| <b>PROJECT CODE</b>    | <EBRL 266>                                                  |
| <b>PROJECT NAME</b>    | EQUITY BANK TANZANIA VODACOM B2C & ATM WITHDRAW INTEGRATION |
| <b>PREPARED BY</b>     | SOSPETER M. MWANIKI                                         |

## **TABLE OF CONTENT**

|          |                                                  |                  |
|----------|--------------------------------------------------|------------------|
| <b>1</b> | <b>Project Initiation Document History .....</b> | <b><u>3</u></b>  |
| 1.1      | Document Location .....                          | <u>3</u>         |
| 1.2      | Revision History .....                           | <u>3</u>         |
| 1.3      | Approvals .....                                  | <u>4</u>         |
| 1.4      | Distribution .....                               | <u>4</u>         |
| <b>2</b> | <b>Project Definition .....</b>                  | <b><u>5</u></b>  |
| 2.1      | Background .....                                 | <u>5</u>         |
| 2.2      | Project objectives and desired outcomes .....    | <u>5</u>         |
| <b>3</b> | <b>Project Approach .....</b>                    | <b><u>6</u></b>  |
| 3.1      | Project scope .....                              | <u>6</u>         |
| 3.2      | Constraints and assumptions .....                | <u>6</u>         |
| 3.3      | Interfaces .....                                 | <u>6</u>         |
| <b>4</b> | <b>Project Management Team Structure .....</b>   | <b><u>7</u></b>  |
|          | <b>Role Descriptions .....</b>                   | <b><u>7</u></b>  |
| 4.1      | ROLES AND RESPONSIBILITIES .....                 | <u>8</u>         |
| 4.2      | TEAM REQUIREMENT MATRIX .....                    | <u>9</u>         |
| <b>5</b> | <b>Quality Management Strategy .....</b>         | <b><u>9</u></b>  |
| 5.1      | Quality standards to be applied .....            | <u>9</u>         |
| 5.2      | Quality Assurance Strategy .....                 | <u>9</u>         |
| <b>6</b> | <b>Risk Management Strategy .....</b>            | <b><u>10</u></b> |
| 6.1      | Risk Management Techniques and standards .....   | <u>10</u>        |
| <b>7</b> | <b>Communication Management Strategy .....</b>   | <b><u>10</u></b> |
| <b>8</b> | <b>Project Plan .....</b>                        | <b><u>11</u></b> |

## 1 Project Initiation Document History

### 1.1 Document Location

The signed copy of this document will be filed at Equity Bank Group Projects File

### 1.2 Revision History

Date of this revision: 16<sup>th</sup> February 2017



Date of next revision:

| Revision date | Previous revision date | Summary of Changes | Changes marked |
|---------------|------------------------|--------------------|----------------|
| 16/02/2017    | None                   | First issue        | 1.0            |

### 1.3 Approvals

This document requires the following approvals.

Signed approval forms shall be filed appropriately in the project filing system.

| Name                | Signature                                                                           | Title                                           | Date of Issue | Version |
|---------------------|-------------------------------------------------------------------------------------|-------------------------------------------------|---------------|---------|
| Joseph Iha          |   | Managing Director -Tanzania                     |               | 1.0     |
| Stephen Macharia    |  | General Manager – Operations                    |               | 1.0     |
| Godwin Mbekelu      |  | ICT- Manager                                    |               | 1.0     |
| Eric Karobia        |                                                                                     | Director for ICT & Data Center                  |               | 1.0     |
| Festus Njuki        |                                                                                     | Director ICT & Data Center                      |               | 1.0     |
| John Wamai          |                                                                                     | Director Enterprise Business System and support |               | 1.0     |
| Moses Mati.         |                                                                                     | Head of Project Programs                        |               | 1.0     |
| Irene Irungu        |                                                                                     | Program Manager                                 |               | 1.0     |
| Sospeter M. Mwaniki |                                                                                     | Project Manager                                 |               |         |

#### 1.4 Distribution

---

| Name             | Title                                           | Version |
|------------------|-------------------------------------------------|---------|
| Joseph Iha       | Managing Director                               | 1.0     |
| Stephen Macharia | General Manager – Operations                    | 1.0     |
| Godwin Mbekelu   | ICT- Manager                                    | 1.0     |
| Eric Karobia     | Director for ICT & Data Centre                  | 1.0     |
| John Wamai       | Director Enterprise Business System and support | 1.0     |
| Moses Mati       | Head of Project Programs                        | 1.0     |



## 2 Project Definition

### 2.1 Background

This project is being undertaken to maximize on our channel networks (ATM's, m-banking, agency), for the Vodacom Money (M-pesa) product. By so doing, Equity Bank Tanzania will be enhancing on deposit collection as Vodacom Tanzania seek to open a collection account with Equity Bank Tanzania, increasing our customer base through conversion of Vodacom customer, growing revenue through the transaction commission to be earned and deepening financial inclusion to the people of Republic of Tanzania through mobile based banking solution.

Vodacom Tanzania Limited is a mobile cellular operator duly licensed to operate a GSM telecommunications system and offer associated value added services such as mobile money to its customers in Tanzania.

Equity Bank Tanzania and Vodacom Tanzania Ltd shall therefore enter into an agreement to offer their respective customers an ATM mobile withdraw and a money transfer solution. The contract is under review and will be one of the project artefacts.

### 2.2 Project objectives and desired outcomes

Some of the major goals/ objectives to be achieved include but are not limited to the following:

- a) Customers with Equity Bank Tanzania accounts will be able to transfer funds from their bank account to Vodacom M-Pesa E-value account (Wallet).
- b) All registered Vodacom M-Pesa customers will be able to withdraw from their Vodacom M-Pesa wallets at any Equity Bank ATM.
- c) Equity Bank Tanzania will grow revenue from B2C and Vodacom M-Pesa ATM withdraw transaction commissions.
- d) Equity Bank Tanzania will mobilize cheap deposit through banking of the Vodacom M-Pesa ATM withdraw collection account.
- e) Equity bank Tanzania will improve the quality of service by allowing registered Vodacom line holders access to their bank accounts through their mobile phones.
- f) Increased usage of our mobile banking application ( Eazzy247)
- g) Increase of the customer base by onboarding the Vodacom subscribers to Equity Bank.

Some of the desired outcomes to be achieved include

- a) The conversion of E-Value held in a Vodacom M- Pesa E-Value Account into Real physical Money;
  - i. Transfer from Bank originating Account to Vodacom M-Pesa E-Value (Wallet);
  - ii. ATM Withdraw from E-Value Vodacom M-Pesa wallet
  - iii. Mobile generated customer bank mini statement and account balance ;

### **3 Project Approach**

#### **3.1 Project scope**

---

The functionalities to be covered in this project are:

- i. Transfer of funds from Equity Bank Tanzania account to Vodacom M-Pesa E-value account (Wallet) via USSD and Eazzy App
- ii. Withdrawal at Equity Bank ATM from Vodacom M-Pesa initiated from USSD and Eazzy App

#### **3.2 Constraints and assumptions**

---

##### **Assumptions**

- EBTL to get more deposits from Vodacom collection Account
- EBTL to increase revenues from B2C and ATM withdraw transaction commission
- No competitor has a similar solution to EBTL at present
- Feedback received during development of the whole phase should be acknowledged and attended to promptly
- Timely decisions to be undertaken on project completion

##### **Constraints**

- EBTL will be dependant to goodwill of Vodacom project team for speedy execution
- EBTL is also dependant on Kenyan team for speed of project
- Bureaucratic administrative procedures

#### **3.3 Interfaces**

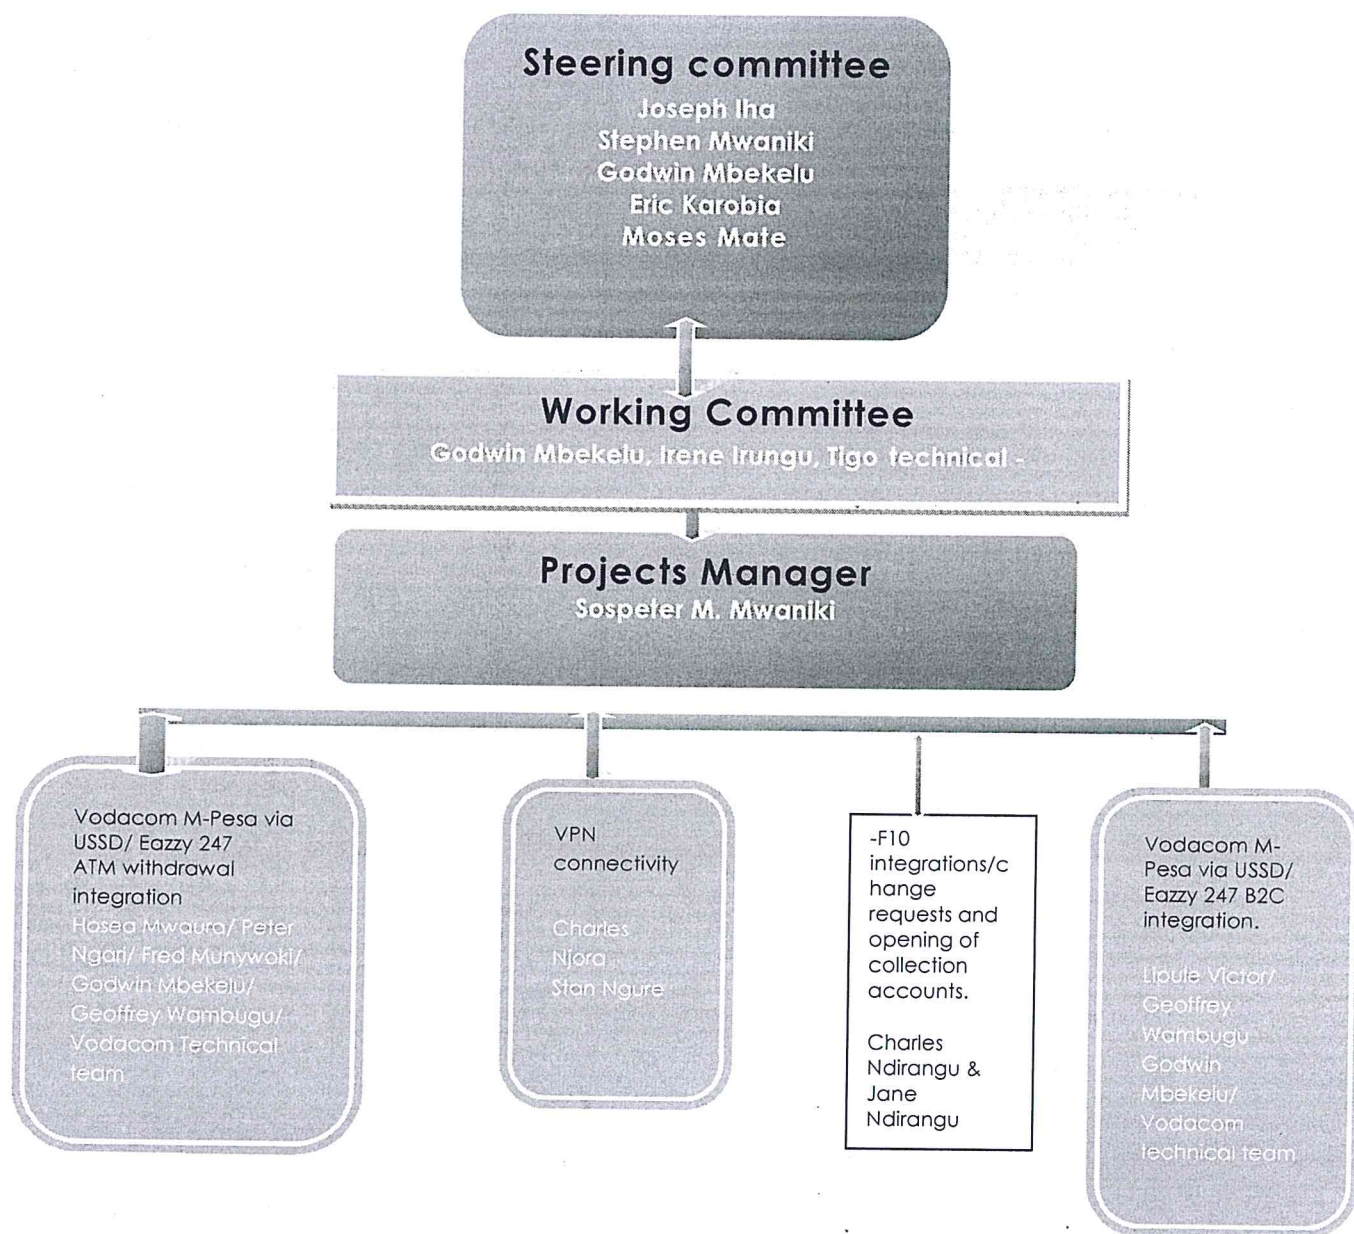
---

Equity Bank networks will play a bigger role in ensuring Equity Bank users get services at any convenient time and place. This will be made available through a successful integration between equity banks and mobile partners Vodacom Tanzania Ltd.



#### 4 Project Management Team Structure

##### PROJECT ORGANISATION STRUCTURE



## Role Descriptions

### 4.1 ROLES AND RESPONSIBILITIES

The roles and responsibilities of the Project Team are detailed below.

#### Steering Committee

- Sets project goals, objectives and strategic direction to the project
- Endorses significant changes in scope and review the performance against set parameters
- Approves policy changes and facilitates Stage wise sign off of documents from the concerned approvers

#### Project Manager

- Ensures that the project requirements are fully defined and understood from the business perspective
- Coordinate joint strategic planning sessions and Supervises key business users roles and responsibilities
- Monitors progress against the plan, Reports regularly to the steering committee and are responsible for change management & process compliance within organization
- Develops detailed Project Plan in consultation with Equity Bank Tanzania Project team contact Assures quality project process and deliverables
- Assesses and monitors risks throughout the project
- Ensure quality of the implementation in line with the Equity Group standards
- Provide guidance on group policies and procedures to ensure uniformity in the implementation

#### Working Team

- Determines the staffing needs of the project and ensures they are met
- Ensures relevant applications knowledge transfer to the Tanzania Functional team
- Develops technical design based on functional requirements document through interaction with functional consultants
- Prepare and deliver quality branding material, communication material Market intelligence



## 4.2 TEAM REQUIREMENT MATRIX

The Teams time requirement shall be as follows;

| ACTIVITY                        | KENYA TEAM TIME (%) | TANZANIA TEAM TIME (%) | GROUP OF USERS FROM EQUITY TANZANIA                                  |
|---------------------------------|---------------------|------------------------|----------------------------------------------------------------------|
| Initiation and Kick-off Meeting | 100                 | 100                    | Managing Director, Head of project Kenya, functional /process owners |
| Training                        | 100                 | 100                    | Process Owners/ Key Users (Training at the head office)              |
| Launch and advertising          | 50                  | 100                    | Process Owners/ Key Users/ Customer Service Representatives          |
| Post Go Live support            | 100                 | 100                    | Process Owners/Key users                                             |

## 5 Quality Management Strategy

### 5.1 Quality standards to be applied

| On                                      | Control Strategy                                                                                                                                                                                                      |
|-----------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Project Scope                           | <ul style="list-style-type: none"> <li>changes to the project time, cost and scope need to be approved and updated to all the project plans and documentation and communicated to stakeholders accordingly</li> </ul> |
| Staff Trainings and System Integrations | <ul style="list-style-type: none"> <li>Acceptance Sign off for the training will be required and as well upon successful SIT and UAT, the system integration acceptance Sign off will be required</li> </ul>          |
| Customer Transactions                   | <ul style="list-style-type: none"> <li>Daily reporting of Transaction and onward reconciliations shall be done</li> </ul>                                                                                             |

### 5.2 Quality Assurance Strategy

For each deliverable throughout the project, the Project Management Team will track and measure quality against the approved standards. Signoffs for every delivery shall therefore be required of Tanzania Team and the Head Office Teams.

## 6 Risk Management Strategy

### 6.1 Risk Management Techniques and standards

RISK LOG AND ISSUE REGISTER SHALL BE MAINTAINED IN DAPTIVE AND UPDATED ON TIMELY BASIS

| Risk                                                          | Probability (H/M/L) | Impact (H/M/L) | Mitigating Action and Costs                                                   | Responsible                |
|---------------------------------------------------------------|---------------------|----------------|-------------------------------------------------------------------------------|----------------------------|
| Availability of partner (Vodacom team) to support the project | H                   | H              | Constant engagement to ensure alignment of tasks and responsibilities         | Vodacom PM                 |
| Network connectivity                                          | H                   | H              | Network infrastructure team to review and guarantee 100% connectivity uptime. | Charles Njora, Stan Ngure, |

| Document Name: EQUITY_RISKLOG.DOC |                |            |                |        |             |          |        |         |
|-----------------------------------|----------------|------------|----------------|--------|-------------|----------|--------|---------|
| SAMPLE Risk Log                   |                |            |                |        |             |          |        |         |
| Risk ID                           | Date Initiated | Risk Title | Date Discussed | Impact | Probability | Category | Status | Remarks |
|                                   |                |            |                |        |             |          |        |         |
|                                   |                |            |                |        |             |          |        |         |
|                                   |                |            |                |        |             |          |        |         |

## 7 Communication Management Strategy

### Project Status Report;

- ❖ A Project Status Report shall be prepared by the Project Management Team Review

### Meetings (Teleconference);

- ❖ There will be regular Project Management review meeting to review the project status & report on any other action points that might come up.

### Meeting Minutes;

- ❖ On completion of the meeting, the Minutes of the Meeting shall be sent out to the Project Stakeholders by the project manager

### Project Plan Update;

- ❖ Project manage will on weekly basis update the Project Plan with actual progress

### Issue Escalation Procedure;

- ❖ The Project Management Board would escalate risk and issues, if any, to the Steering committee

## 8 High Level Project Plan

| Milestones/Deliverables              | Target Start Date | Target End Date   |
|--------------------------------------|-------------------|-------------------|
| Project Initiation & Project Charter | February 23, 2017 | March 2, 2017     |
| Project Plan Review and Completion   | February 24, 2017 | February 25, 2017 |
| Project Kickoff                      | March 3, 2017     | March 3, 2017     |
| Contract Sign off                    | March 3, 2017     | March 23, 2017    |
| Project Requirement Definition       | March 3, 2017     | March 23, 2017    |
| Project Design                       | April 3, 2017     | May 12, 2017      |
| Project Build                        | May 12, 2017      | June 14, 2017     |
| Project testing                      | June 14, 2017     | July 20, 2017     |
| Business Preparedness Check          | July 20, 2017     | August 7, 2017    |
| Go live                              | July 20, 2017     | August 7, 2017    |
| Project Closure                      | August 7, 2017    | August 21, 2017   |
